Evansville MPO
Henderson • Vanderburgh • Warrick

Pamela Drach
Executive Director

TO: Technical Committee Members

FROM: Pamela Drach, Executive Director

DATE: September 3, 2026

The Technical Committee meeting is scheduled for **Thursday, September 10, 2026 at 10:00 a.m. CST/ 11:00 am EST in Room 318 of the Civic Center Complex 1 NW Martin Luther King Jr. Blvd. Evansville, IN 47708.**

AGENDA

1. **Roll Call**

2. **Approval of Minutes**

3. **Old Business**
   a. Project Update

4. **New Business**
   a. 2026-2030 Transportation Improvement Program (TIP) Modifications (Informational)
   b. 2026-2030 Transportation Improvement Program (TIP) Amendments (Approval Requested)
   c. FY 2032 Indiana Call for Projects (Approval Requested)

5. **Other Business**
   a. Lloyd4All presentation - Stantec
   b. Mobility Stats

6. **Public Comments**

7. **Upcoming Dates**
   CY 2026 EMPO Technical Meetings: September 10, November 12, 2026

8. **Adjournment**

PD/KA

The EMPO will provide reasonable accommodations to individuals with a disability or who require language assistance that wish to attend this meeting. Because this may require outside assistance, please make requests at least one week prior to the meeting day by calling the MPO office at 812-436-7833, by email at jscott@evansvillempo.com, or by writing to: Evansville MPO, Civic Center Complex Room 316, 1 N.W. Martin Luther King, Jr. Blvd, Evansville, Indiana 47708.

Pamela Drach
Executive Director

EVANSVILLE METROPOLITAN PLANNING ORGANIZATION
TECHNICAL COMMITTEE MINUTES

Regular meeting held at 10:00 a.m. in Room 318
Civic Center Complex – Administration Building
Evansville, Indiana

July 9, 2026

The following are minutes and not intended to be a verbatim transcript. An audio version of the proceedings can be heard or viewed on our website at www.evansvillempo.com.

1. ROLL CALL

Members Present:

Technical Members	Organization	In Person	Webex/ Phone
Luke Hill	INDOT	X	
Nick Hall	KYTC	X	
Jessica Waddle	KYTC	X	
Thomas Witt	KYTC	X	
Emily Deason	KYTC	X	
Tobin Maxfield	KYTC	X	
Samantha Fleischaker	Evansville Human Resources Commission	X	
Nate Hahn	EVV Regional Airport		X
David Broderhausen	INDOT		X
Karen Brooks	Easterseals Rehabilitation Center		X
Jay DuMontelle	FHWA		X
Shawn Hayden	Eastland Mall		X
Cinda Phillips	Arc of Evansville		X
Camille Robinson	FHWA		X
Steve Roelle	Success Warrick County		X
Lorie Van Hook	Evansville Trails Coalition		X

Evansville MPO Staff Present:

EMPO Staff	In Person	Webex/ Phone
Pam Drach	X	
Matt Schriefer	X	
Erin Schriefer	X	
Jennifer Scott	X	
Kari Akin	X	
Lorenzo Marsh	X	

Nate Hahn directed the meeting.

2. APPROVAL OF MINUTES

Lorie Van Hook made a motion for approval and Steve Roelle seconded the motion; motion carried.

3. OLD BUSINESS

a. Project Update – presented by Jennifer Scott

Project	Description	Most Current Status Information
Vanderburgh County		
Oak Hill Rd: Lynch Rd to St George Rd	Road widening with bike and pedestrian accommodations	Construction activities are ongoing. Utility relocation work and storm sewer installation is continuing. The contractor will begin installing new waterline along Oak Hill Rd between Eastbrooke Dr west and Aspen Dr during the week of July 6.
Petersburg Rd: Clubhouse Dr to Boonville New Harmony Rd	Road reconstruction with multi-modal improvements	The Commissioners approved a resolution for this amended contract on 5/26/26. It will have to be approved by the County Redevelopment Commission next, but no date has been set for that meeting. This is not preventing the design work from continuing.
Wimberg Rd: Bridge over Locust Creek	Bridge replacement	The 401 and 404 permits were approved on 6/23/26. Right-of-way acquisition is continuing. One parcel still needs to be acquired. Utility coordination and final design are continuing.
Warrick County		
Epworth Rd Phase 1: Tecumseh Dr to south of SR 66	Road widening with bike and pedestrian accommodations	24 of the 25 parcels have had offers accepted. MOT coordination with City of Evansville, INDOT, and the hospital is ongoing. Stage 3 plans submitted on 5/22/26. Utility work plans being finalized. Permit applications being finalized. 401 permit approved on 6/22/26.
Epworth Rd Phase 2: SR 662 to Tecumseh Dr	Road widening with bike and pedestrian accommodations	Historic Properties Short Report submitted to consulting parties for review and comment on 6/9/26. Working with the cemetery property owner to schedule field work.
Oak Grove Rd Phase IV: SR 261 to Anderson Rd	Road widening with bike and pedestrian accommodations	Received approval to submit draft environmental document before having MPPA approval. INDOT will check on the status of the MPPA review and approval. Right-of-way engineering finalized on 5/29/26 and appraisal analysis has begun.

INDOT Updates – presented by Luke Hill

Contract	Project	Description	Most Current Status Information
INDOT			
R-44898	SR 66 At 1.79 mi E of US-41 (Vann Ave)	Intersection Improvement	Installed Enduroblend color to curbs at Stockwell. Completed closer work at Burkhardt, continuing concrete work at Cross Pointe and Burkhardt.
	SR 66 At 1.20 mi W of I-69 (Burkhardt Rd)	Intersection Improvement	
	SR 66 At 0.58 mi W of I-69 (Cross Pointe Blvd)	Intersection Improvement	
	SR 66 At 2.25 mi E of US 41 (Stockwell Rd)	Intersection Improvement	
R-42287	SR 62 Pedestrian Walk at SR-62 EB/WB	Bridge Replacement	Opened University Parkway Ramps. Working on Red Bank & Rosenberger Southern Approaches. Continuing to work on bridges and Eastbound Pavement.
	SR 62 At 6.62 mi W of US-41 (Schutte Rd)	Intersection Improvement	
	SR 62 At 4.58 mi W of US-41 (Rosenberger Ave)	Intersection Improvement	
	SR 62 From Rosenberger Rd (4.59 mi W of S Jct US-41) to 3.92 mi W of S Jct US-41 (Ingle Ave)	Road Reconstruction (3R/4R Standards)	
	SR 62 From 8.56 mi W US 41 to 4.59 mi W of US 41 (East of Posey/Vanderburgh Count Line to Rosenberger Rd	Rubblize PCCP & HMA Overlay	
	SR 62 At McDowell Road, 7.75 mi W of US41	Intersection Improvement	
R-45152	SR 62 from 3.92 mi W of S Jct US 41 (Ingle Ave) to 2.72 mi W of Jct US 41 (Wabash Ave)	Pavement Replacement	Utility relocations are underway. Construction will be starting tentatively in August or September.
	SR 62 At 3.09 mi W of US-41 (St. Joseph Ave.)	Intersection Improvement	
	SR 62 2.72 mi W of US 41 (Wabash Ave)	Intersection Improvement	

R-45753	US 41 0.66 miles S of SR 57 at Petersburg Rd	Intersection Improvement	Railroad coordination nearing completion and found an additional right-of-way parcel owned by Centerpoint, and will not go in condemnation. We may need to push this project back a month or two to avoid letting with exceptions. FInal Field Check Scheduled for July 14th.
R-44013	SR 62 (Morgan Ave.) At Boeke Road, 1.01 mi E of US 41	Intersect. Improv. W/ Added Turn Lanes	A tree is going to get put on a maintenance contract and will be cut down this Fall/Winter then utility relocations will follow, may have to let with exceptions. Working towards final tracings on Boeke. On Stockwell, we are waiting for the liquor store to move their sign (by September 1st) and we are working towards final tracings. Environmental documentation completed for the bridge over Harper Ditch. Working towards final tracings.
	SR 62 At Stockwell Road, 2.01 mi E of US 41	Intersect. Improv. W/ Added Turn Lanes	
	SR 62 SR 62 Bridge over HARPER DITCH, 01.78 mi E US 41	Bridge Deck Overlay	
R-45274	From 3.30 mi N SR-57 (0.20 mi N Boonville/New Harmony Road) to 0.85 mi S. SR 168 (0.20 mi N. Coal Mi	Rubblize PCCP & HMA Overlay	Environmental Document has been submitted for review. Utility Coordination is progressing and geotech work is almost completed.
	From 3.30 mi N SR-57 (0.20 mi N Boonville/New Harmony Road) to 0.85 mi S. SR 168 (0.20 mi N. Coal Mi	Small Structures & Drains Construction	
	US 41 NB over Pond Flat Ditch 02.01 miles S of I-64	Bridge Replacement	
	US 41 SB over Pond Flat Ditch 02.01 miles S of I-64	Bridge Replacement	
R-44500	SR 66 2.23 miles W of SR 65 at University Parkway Intersection	Intersection Improvement	For SR 57 in Daylight, confirmed with the county to use Boonville-New Harmony Road a detour route. Maintenance of Traffic is to be a closure with business access. Stage 2 is complete under consultant review.
	SR 57 3.36 mi S of I-69 (N. Green River Rd. Intersection)	Intersection Improvement	
	SR 57 3.36 mi S of I-69 (N. Green River Rd. Intersection)	ADA Sidewalk Ramp Construction	
R-39923	US 41 At Lynch Road, 1.0 mi N of SR-66	Intersection Improvement. Added left turn lane on SB US 41. No improvements on Lynch other than resurface.	Railroad coordination and utility coordination is on-going. Environmental meeting took place in March to try and limit impacts to require a lower level environmental document.
R-45035	SR 62 1.50 mi W of I-69 (Green River Rd)	Other Intersection Improvement	Met with the City to go over options for access control. Working on incorporating that discussion into the plans.
R-45795	SR 61 4.62 mi S of SR 62 (Roeder Rd./CR 300 S)	Intersection Improvement, Roundabout	Early Coordination Letters sent out. Working towards a stage 1 submittal. Early concerns with the amount of Right of Way involved.
R-44499 (Des# 2200044)	US 41 1.57 miles S of SR 57 At St. George Road	Intersection Improvement	Working through 3 design alternatives to see which would have the best cost-benefit analysis.
R-46317	Walnut St. and Lincoln Ave and Bellemeade Avenue in Evansville	Intersection Improvement	Developing preliminary layouts for the alternatives. Starting the section 106 for the environmental field work. A meeting will take place to discuss traffic analysis, alternates, crash analysis and cost estimates. Will be scheduling a scoping field check soon. Continued work on utility coordination.

Nate Hahn asked if INDOT could share the design alternative concepts for the US 41 and St George Rd project with EVV Regional Airport for coordination between INDOT and the airport. The airport has long-term plans and wants to make sure everyone is on the same page moving forward. Luke Hill responded that he would send the alternatives to Nate.

This item was informational and did not require committee action.

4. NEW BUSINESS

a. 2023-2030 TIP Modifications – presented by Erin Schriefer

The Evansville MPO modified the FY 2026-2030 Transportation Improvement Program with the following:

Date Processed	Sponsor	Contract	Des#/ID#	Road	Description	County	Work Type	Funding Type	% Split	Action	Fiscal Year	Phase/ Source	Current TIP Entry	New TIP Entry Total	New TIP Entry Federal	New TIP Entry State/Local
													All amounts in thousands			
26-May-26	KYTC	N/A	02-943	KY 416	Signing improvements from MP 10.7 to MP 15.7	Henderson	Highway Signage	HSIP	100%	Add Project	2026	CN	$0	$132	$132	$0
					Grouped Project: (Highway Signage)											
2-Jun-26	INDOT	46482	2501126	Various	Various locations in the Vincennes District	Various	District Wide Bridge Maintenance	BR	80/20	Revise Funding	2027	CN	$1,000	$2,000	$1,600	$400
					Grouped Project: (Bridge, Culvert and Small Structure Preservation)						2028	CN	$0	$2,000	$1,600	$400
2-Jun-26	INDOT	46290	2500801	SR 62 & SR 66	Intersections with Epworth Rd, Bell Rd, and SR 61	Warrick	Intersection Improvement Median U Turn	HSIP	80/20	Move FY & Revise Funding	2026	PE	$1,900	$0	$0	$0
					Includes Des# 2500799, 2500800						2027	PE	$0	$2,134	$1,707	$427
18-Jun-26	INDOT	46290	2500801	SR 62 & SR 66	Intersections with Epworth Rd, Bell Rd, and SR 61	Warrick	Intersection Improvement Median U Turn	HSIP	80/20	Revise Funding	2027	PE	$2,134	$2,764	$2,211	$553
					Includes Des# 2500799, 2500800											
													All amounts in millions			
23-Jun-26	INDOT/KYTC	N/A	1601700, 2300092, 02.1088.5, 1088.52	I-69	Interstate 69. Section 2: New four-lane river crossing	Henderson/ Vanderburgh	New Bridge Construction	KY NH IN NHPP KY Garvee IN NHPP		Revise FY and Funding	2027	CN	$543	$285	KY: $41 IN: $60	KY: $158 IN: $26
											2028	CN	$104	$362	KY: $104 IN: $180	KY: $0 IN: $78
													All amounts in thousands			
6-Jul-26	KYTC	N/A	02-9030.00	US 41	BMP: 16.450 to EMP: 16.660	Henderson	Installation of High Friction Surface on US 41	HSIP	90/10	Add Project	2027	CN	$0	$180	$162	$18
					Grouped Project: (Pavement resurfacing, restoration, and rehabilitation projects)											

This item was informational and did not require committee action.

b. 2026-2030 TIP Amendments – presented by Erin Schriefer

The Evansville MPO amended the FY 2026-2030 Transportation Improvement Program with the following:

Sponsor	Contract	Des#/ID#	Road	Description	County	Work Type	Funding Type	% Split	Action	Fiscal Year	Phase/ Source	Current TIP Entry	New TIP Entry Total	New TIP Entry Federal	New TIP Entry State/Local
												All amounts in thousands			
Evansville	T-45893	2401669	Various	on Diamond Ave, Covert Ave and Lynch Rd	Vanderburgh	Installation of radar speed limit feedback systems	HSIP	-	Remove from TIP	2027	CN	$92	$0	$0	$0
Evansville	T-45919	2401664	Franklin St	from Fulton Avenue to First Avenue	Vanderburgh	Road reconfiguration to reposition travel lanes, parking, and multiuse path	HSIP	-	Remove from TIP	2027	CN	$166	$0	$0	$0
Evansville	T-45897	2401668	John St	at Governor Street and Garvin Street	Vanderburgh	Installation of Stop Ahead & Other pavement markings, LED Stop signs, and curb bump outs	HSIP	-	Remove from TIP	2027	CN	$212	$0	$0	$0

Steve Roelle made a motion for approval and Shawn Hayden seconded the motion; motion carried.

c. MPO Planning Area Roadway Functional Classification Changes – presented by Matt Schriefer

The Evansville MPO is submitting updates to the MPO Planning Area Roadway Functional Classification system for INDOT and FHWA approval. Following the decennial census, the MPO updates roadway classifications to integrate updated urban boundaries and ensure the designations accurately reflect the function of the roadway within the regional network. The recommended changes were developed in coordination with city and county engineers.

Route	StartPoint	EndPoint	Jurisdiction	Current Functional Class	Proposed Functional Class
1ST ST	MAIN ST	NORTH ST	Elberfeld	Major Collector	Local
2ND ST	MAIN ST	NORTH ST	Elberfeld	Local	Major Collector
MAIN ST	2ND ST	1ST ST	Elberfeld	Local	Major Collector
BARKER AVE	TERMINUS	BROADWAY AVE	Evansville	Major Collector	Local
BURKHARDT RD	TERMINUS	WASHINGTON AVE	Evansville	Major Collector	Local
COVERT AVE	GOVERNOR ST	GARVIN ST	Evansville	Major Collector	Local
GARVIN ST	RIVERSIDE DR	COVERT AVE	Evansville	Local	Major Collector
KENTUCKY AVE	PFEIFFER RD	MILL RD	Evansville	Local	Minor Collector
PFEIFFER RD	STRINGTOWN RD	KENTUCKY AVE	Evansville	Local	Minor Collector
SR 61	SR 62	OLD SR 61	INDOT	Local	Minor Arterial
ELLERBUSCH RD	SR 662	NEWBURGH CITY LIMIT	Newburgh	Local	Minor Collector
JEFFERSON ST	JENNINGS ST	STATE ST	Newburgh	Minor Arterial	Major Collector
STATE ST	JENNINGS ST	JEFFERSON ST	Newburgh	Major Collector	Minor Arterial
BROWNING RD	BOONVILLE-NEW HARMONY RD	OLD STATE RD	Vanderburgh	Minor Collector	Major Collector
GREEN RIVER RD	SR 57	PETERSBURG RD	Vanderburgh	Local	Minor Collector
LAKE SHORE DR	TERMINUS	NEW HARMONY RD	Vanderburgh	Major Collector	Local
LAUBSCHER RD	TERMINUS	KRATZVILLE RD	Vanderburgh	Major Collector	Local
MT PLEASANT RD	DARMSTADT RD	US 41	Vanderburgh	Local	Major Collector
OLD STATE RD	INGLEFIELD RD	VANDERBURGH COUNTY LINE	Vanderburgh	Minor Collector	Major Collector
PETERSBURG RD	BOONVILLE-NEW HARMONY RD	SR 57	Vanderburgh	Local	Minor Collector
SEIB RD	KANSAS RD	BOONVILLE-NEW HARMONY RD	Vanderburgh	Local	Minor Collector
STRUEH-HENDRICKS RD	POSEY COUNTY LINE RD	BROADWAY AVE	Vanderburgh	Local	Major Collector
ANDERSON RD	SHARON RD	JENNER RD	Warrick	Local	Major Collector
ASBURY CEMETERY RD	HEIM RD	NEW HARMONY RD	Warrick	Local	Minor Collector
CASEY RD	VANN RD	TERMINUS	Warrick	Minor Collector	Local
ELLERBUSCH RD	NEWBURGH CITY LIMIT	WILLOW POND RD	Warrick	Local	Minor Collector
EPWORTH RD	SR 662	SR 62	Warrick	Major Collector	Minor Arterial
GRIMM RD	SR 662	WARRICK TRL	Warrick	Local	Major Collector
HILLSBORO DR	VANN RD	SR 261	Warrick	Local	Major Collector
JENNER RD	CASTLE GARDEN RD	ANDERSON RD	Warrick	Local	Major Collector
LENN RD	LINCOLN AVE	TERMINUS	Warrick	Major Collector	Local
LIBBERT RD	SR 66	TELEPHONE RD	Warrick	Local	Major Collector
LINCOLN AVE	SR 66	ANDERSON RD	Warrick	Minor Collector	Major Collector
ROCKPORT RD	BULLOCKTOWN RD	BROWN CHAPEL RD	Warrick	Local	Minor Collector
ROEDER RD	SR 61	YANKEETOWN RD	Warrick	Local	Minor Collector
SHARON RD	SR 66	ANDERSON RD	Warrick	Minor Collector	Major Collector
TENNYSON RD	PARKLANE DR	FRANZ RD	Warrick	Local	Minor Collector
VANN RD	LIBBERT RD	HILLSBORO DR	Warrick	Local	Major Collector
WARRICK TRL	EPWORTH RD	LIBBERT RD	Warrick	Local	Major Collector
WILLOW POND RD	GRIMM RD	FRAME RD	Warrick	Local	Minor Collector

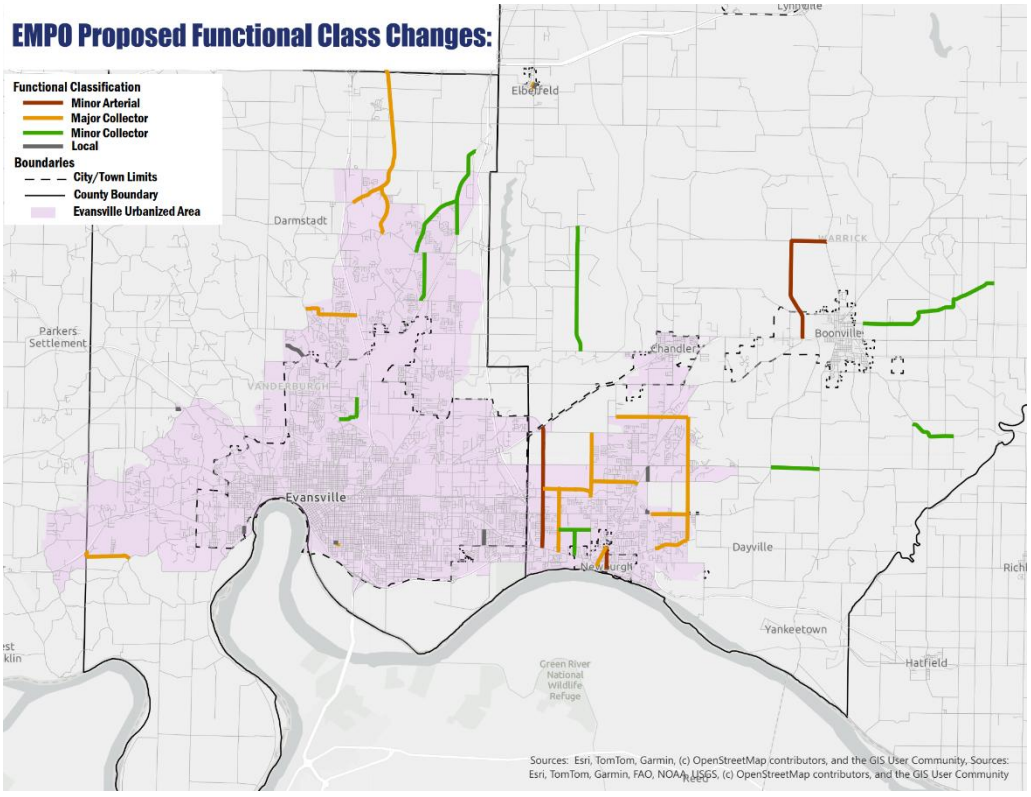

Lorie Van Hook made a motion for approval and Steve Roelle seconded the motion; motion carried.

5. OTHER BUSINESS

a. Mobility Hubs – presented by Matt Schriefer

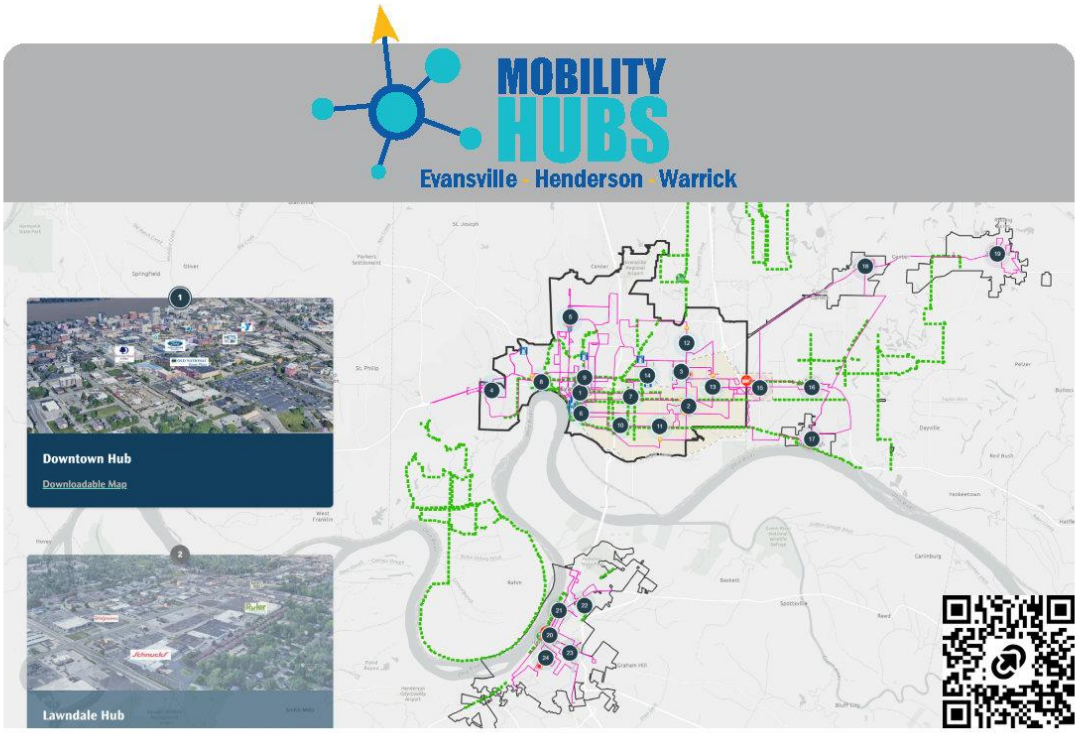

What is a Mobility Hub?

A Mobility Hub is a neighborhood and/or commercial hub that includes a concentration of bus, bike, and pedestrian infrastructure.

What's Included in a Mobility Hub?

Think of it as a neighborhood center where the following come together:

- **Public Transit:** METS, HART, and WATS bus routes.
- **On-Demand Rides:** The METS Micro zone.
- **Pedestrian & Bike Paths:** Sidewalks, trails, and bike lanes.
- **Shared Wheels:** Upgrade Bikeshare stations and electric scooters.

Why do they matter?

1. **Seamless Connections:** They make it easy to switch from a bus to a bike or a scooter without a hassle.
2. **Future-Proofing:** These spots are the priority zones for new upgrades, like better sidewalks, more trails, and EV charging stations.
3. **Regional Access:** The ultimate goal is to create a network of these hubs, allowing you to travel across the entire region without needing a personal car.

For more information: https://tinyurl.com/mobilityhubs

Matt Schriefer explained what a Mobility Hub is, how they were identified, and their importance. He showed the interactive map that has been created. Nate Hahn commended the MPO for trying to make this information as transparent as possible and making it easily accessible for the community.

b. Mobility Stats – presented by Matt Schriefer

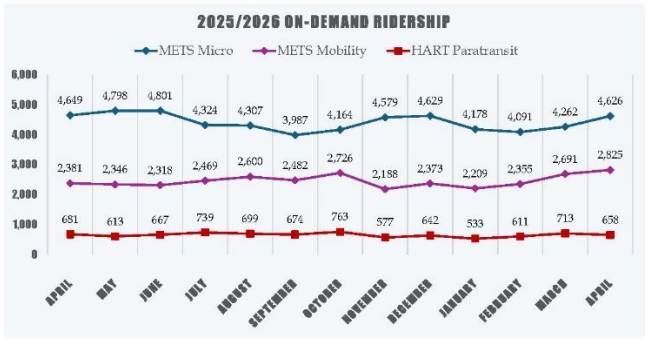

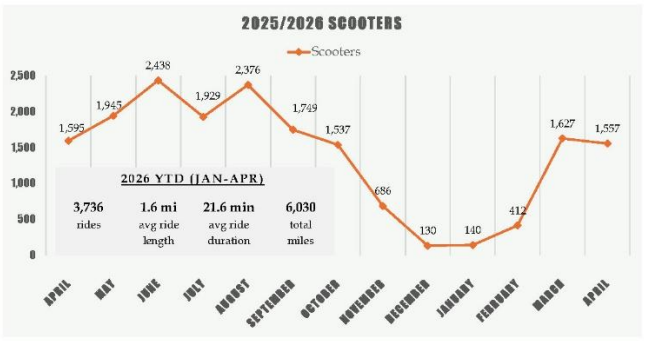

Matt Schriefer explained that the MPO is working with METS, HART, and the Evansville Trails Coalition to gather usage data monthly. He briefly walked through the data and the trends that are being seen. Matt also provided a flyer from the Evansville Trails Coalition that had more detailed bikeshare numbers (the flyer is on the next page).

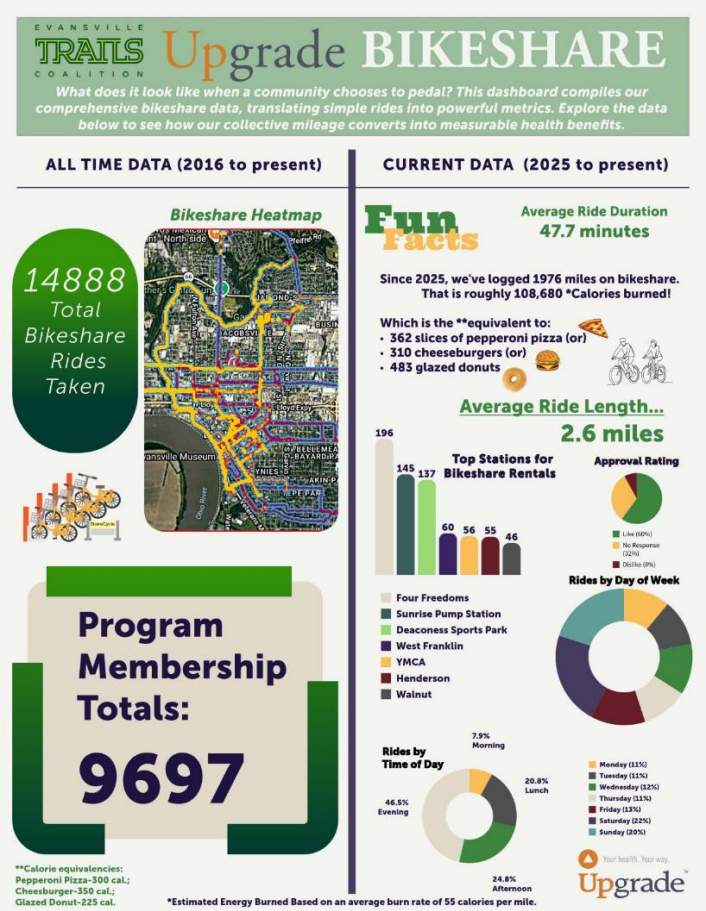

6. PUBLIC COMMENTS

Erin Schriefer announced that within the next week or so, the MPO will be sending out a Call for Projects for Federal Highway funding for Indiana projects for FY 2032. This means projects will have to be ready to go to letting between July and November 2031. The application and guidance document will be distributed with the call announcement. Applications will be due back to the MPO in the first week of August. All details will be included in the call announcement.

Thomas Witt (KYTC) announced that KYTC recently completed the 2026 Enactive Highway Plan and it is available on their website. In looking at the plan, it looks like there are a few new projects in Henderson County, and some changes to existing projects. KYTC will be working with the MPO to update the TIP and MTP as necessary to reflect the new Enactive Highway Plan.

Kari Akin announced that Nick Hall (KYC) is retiring and that this will be his last MPO meeting. Nick Hall said it has been great working with everyone over the years.

7. UPCOMING DATES

- CY 2026 EMPO Technical Meetings:
  - September 10
  - November 12

Meeting adjourned.

Updates on Funded LPA Projects: Indiana

Sep-26

Project Sponsor	Project	Description	Preliminary Engineering/ Design: Consultant Selection & NTP	Preliminary Engineering/ Design: Preliminary Field Check	Preliminary Engineering/ Design: Pubic Hearing / Meeting Notice	Preliminary Engineering/ Design: Environmental Approval	Right-of-Way: Right of Way Acquisition	Design: Final Tracings	Construction: Bid Letting/ Award	Construction: Construction	Most Current Status Information
City of Evansville	**Third Street**: from Court St to Parrett St	Road reconstruction with multi-modal improvements.	Complete	Ongoing							Preliminary Engineering (PE) contract awarded to VS Engineering. NTP has been issued to VS and survey is underway. Consultant revising design contract to reflect phasing the project: Court to Walnut as PH1 and Walnut to Parrett as PH2.
Vanderburgh County	**Oak Hill Rd** from Lynch Rd to St George Rd	Road widening with bike and pedestrian accommodations	4/1/21	12/9/21	Complete	5/1/24	Complete	Complete	1/14/26	Ongoing	Project was let for bid on 1/14/26. The contract has been awarded to Blankenberger Brothers, Inc. in the amount of $9,756,450. The preconstruction meeting will be held on March 11. Right-of-way clearing has started. ***Construction activities are ongoing. Utility relocation work and storm sewer installation is continuing. The new waterline installation along Oak Hill Road between Eastbrooke Drive west and Aspen Drive and Bergdolt Road is ongoing. Roadway reconstruction started in mid-July and is progressing well. Work is continuing on the storm sewer, water main and water services lines, and full width/depth roadway reconstruction.***
	Petersburg Rd from Clubhouse Dr to Boonville New Harmony Rd	Road reconstruction with multi-modal improvements.	Complete								The County is currently working on updating the scope of the Structurepoint contract so that it matches the new project schedule. ***The Redevelopment Commission approved the use of Burkhardt Road TIF funds on the Structurepoint contract amendment at their 9/2/26 meeting. Final approval of the contract will be on the agenda for the 9/15/26 Commissioners' meeting.***
	Wimberg Rd Bridge over Locust Creek	Bridge replacement	6/1/23	8/2/24	Complete	Ongoing	Ongoing				PE contract awarded to Beam Longest and Neff. Notice to Proceed given 6/1/23. The hydraulic analysis was completed and the alignment was set to allow phased construction at the site. The structure, size and type study is underway to determine the most cost effective structure. Centerpoint Gas to proceed with acquiring a utility easement. Adjustments to the r/w limits are being evaluated to avoid conflicts with a gas monitoring valve on the landfill parcel. Adjustments are also being evaluated to reduce the r/w acquisition on the other parcel being acquired for this project. Utility work plans have been submitted. Environmental approval was received on 1/28/2026. Public involvement has been certified. Stream and wetland mitigation credits have been.purchased. The 401 and 404 permits were approved on 6/23/26. ***Utility coordination is continuing on the relocation of the force main. One right of way parcel needs to still be acquired. Final design work is continuing.***
Warrick County	**Telephone Rd**: Bell Rd to Fuquay Rd	Road widening with bike and pedestrian accommodations	12/19/19	4/15/21	2/1/22	4/21/22	Complete	Complete	7/10/24	Ongoing	Project was let for bid on July 10 with low bid of $8.82M received from Blankenberger Brothers Inc. BBI is working on completing subgrade operations between Coal Mine and Fuquay. Storm is close to being completed on Fuquay. Asphalt (except surface), curb and gutter, and drives are complete from Bell to, and including, Coal Mine. ***Project is nearing completion and opened to traffic the week of 8/3/26.***
	Epworth Rd Phase 1: from Tecumseh Dr to south of SR 66	Road widening with bike and pedestrian accommodations	7/26/22	9/18/24	5/2/25	8/7/25	Complete		*1/13/27*		PE contract awarded to Lochmueller Group. A kick-off meeting was held on October 11, 2022. Draft Traffic Study, Hydraulic Study, and Archeology Study completed. Preliminary Field Check held Sept 18, 2024. Public information meeting held 1/22/25. Public Involvement Certification and Environmental document approved 5/29/25. ***MOT coordination with the City of Evansville and hospital is ongoing. Utility coordination is ongoing and utility work plans being finalized. 404 permit application being finalized. Stage 3 plans were submitted on 5/22/26 and reviewed by INDOT. 401 permit application was approved on 6/22/26. CSGP approved on 7/13/2026. All right-of-way has been acquired. Final Field check was held on 8/18/26.***
	Epworth Rd Phase 2: from SR 662 to Tecumseh Dr	Road widening with bike and pedestrian accommodations	4/7/25	Ongoing		Ongoing					Request for Proposals for preliminary engineering posted with responses due Nov 12, 2024. PE contract awarded to Lochmueller Group. Notice to proceed issued 4/7/25. Initial Section 106 coordination with Archeologist and Historian is underway. The Draft Early Coordination Letter and Cemetery Development Plan was submitted and reviewed by INDOT Cultural Resources Office. The Consultant addressed the comments received and resubmitted the document on 12/3/25. The Archaeological Work Plan was submitted to and reviewed by INDOT Cultural Resources Office. The Consultant addressed the comments received and resubmitted the document on 2/4/26. ***Historic Properties Short Report submitted to Consulting Parties for review and comment on 6/9/26. Working with the Cemetery property owner to schedule field work. Environmental is ongoing. Preliminary Design Plan Development ongoing.***
	Oak Grove Rd Phase IV: From SR 261 to Anderson Rd	Road widening with bike and pedestrian accommodations	1/10/24	1/28/25	Ongoing	Ongoing					PE contract awarded to Lochmueller Group. Notice to Proceed with design issued to the Consultant 1/10/24.Topography survey nearing completion. Subsurface utility engineering to begin in May. PE and environmental tasks started. Utility engineering is ongoing. Preliminary Field Check held 1/28/25. Geotech field investigation started 2/3/25. Public Information Meeting held August 7th. Design revisions are being considered based on feedback received at the meeting. Utility coordination ongoing. ***MPPA approved. Draft Environmental Document submitted on 5/19/26. Right-of-way engineering finalized on 7/31/2026 and appraisal analysis is ongoing. Utility Coordination is ongoing.***

Dates Non-italicized dates reflect the completion date for the activity,
Italicized dates reflect anticipated completion dates for the activity, where appropriate.

Updates on Funded Projects: Kentucky

Sep-26

Project Sponsor	Project	Description	Preliminary Engineering/ Design: Professional Services Procurement	Preliminary Engineering/ Design: Preliminary Line and Grade Plans	Preliminary Engineering/ Design: Pubic Meeting / Meeting Notice	Preliminary Engineering/ Design: Environmental Approval	Right-of-Way: Right of Way Acquisition	Design: Construction Procurement Package	Construction: Bid Letting/ Award	Construction: Construction	Comments
KYTC	**Watson Lane** from Sunset Ln to Green River Rd	Improve safety and reduce congestion.	1/29/19	6/6/19	9/16/19	10/30/20	Ongoing				The Phase 1 plans are complete and an alternative has been selected. Federal authorization has been received for the second phase of design. Joint inspection meeting held October 28th. Project split into 2 sections/phases with the intersection improvement phase a priority. Updated RW plans were submitted the end of April. Utility agreements are in place and the utility plans have been requested and are due for submittal in October. RW acquisition process underway with offers being made.
	KY 2183 and KY 1539	Intersection project to improve safety.	n/a	Ongoing							Design plan revisions, to minimize utility impacts and costs, are being discussed. The City and County are reviewing the project purpose, need, benefits and costs to identify a preferred alternative. The County is reviewing low volume roundabout design options for potential impacts to the utilities at the intersection, particularly impacts to the gas line. Additional options were discussed during a KYTC/LPA/MPO meeting in August. Further discussions are needed to determine the viability of the options. Current project scope includes purchasing right-of-way to maintain appropriate intersection sight distance. KYTC design section is working on determining the size of the sight distance triangles to develop costs estimates for potential acquisition.

Dates Non-italicized dates reflect the completion date for the activity,
Italicized dates reflect anticipated completion dates for the activity, where appropriate.

Updates on Funded INDOT Projects in MPO area

Sep-26

					Preliminary Engineering/ Design				Right-of-Way	Design	Construction		
Des	Contract	Project Manager	Project	Description	Consultant Selection & NTP	Preliminary Field Check	Public Hearing / Meeting Notice	Environmental Approval	Right of Way Acquisition	Final Tracings	Bid Letting/ Award	Construction	Most Current Status Information
1900268	R-44898	Bullock, Matthew	SR 66 At 1.79 mi E of US-41 (Vann Ave)	Intersection Improvement	Complete	3/9/2022	8/1/2022	Complete	Complete	Complete	1/18/24	On-going	Contract was awarded to JBI for $35,498,919.88. Pre-Construction meeting held 2/22/24. Stockwell was completed and open to the public in June 2025. Contractor is working on Pre-phase work in the center of the Lloyd at Burkhardt. Southside, Eastbound lane of the Lloyd will be closed soon for approx. 4 months. During this closer right turns onto and off of the Lloyd from Burkhardt & Cross Pointe will be periodically restricted. Lane restrictions in place at Burkhardt, Two week notice for right turn closure and lane restrictions at Cross Pointe went out 9/4. Added epoxy pavement marking to Stockwell to improve visibility, will also add Temp Raised pavement markings. In Phase 2 MOT. Working on overhead wiring for traffic signals. Working on pavement removal and subgrade treatment. Installed Enduroblend color to curbs at Stockwell. Completed closer work at Burkhardt, continuing concrete work at Cross Pointe and Burkhardt. **Traffic has shifted to the outside and Westbound displaced turns are operational. Continuing to work in the median.**
1900292			SR 66 At 1.20 mi W of I-69 (Burkhardt Rd)	Intersection Improvement				Complete	Complete				
1900317			SR 66 At 0.58 mi W of I-69 (Cross Pointe Blvd)	Intersection Improvement				Complete	Complete				
2000217			SR 66 At 2.25 mi E of US 41 (Stockwell Rd)	Intersection Improvement				Complete	Complete				
1702066	R-42287	Bullock, Matthew	SR 62 Pedestrian Walk at SR-62 EB/WB	Bridge Replacement	Complete	Complete	Complete	Complete	Complete	Complete	3/27/24	On-Going	Project was awarded to Ragle and E&B Joint Venture for $142,459,537.95, Asphalt was the winning pavement type. Pre-Construction Meeting was scheduled for 5/2/24. Demo of Railroad bridge is ongoing. Contractor is installing T-Wall at Carpenter Creek Bridge. Roadway foundation earthwork is ongoing. Open Graded Asphalt, the base layer is being placed on mainline pavement. Middle Mount Vernon Rd north of the Lloyd will close 7/7 for 14 days. Boehne Camp Rd north of the Lloyd will close 7/14 for 30 days. Beams have been set at Tekoppel & Carpenter Creek Bridges. Work on walls at CSX bridge is ongoing, plan to place beams 10/2. Will move traffic West of Red Bank to the north side (Westbound lanes) on or after 9/8. Work on pedestrian bridge between Lemke and St Joe will begin second week in October, some pre-phase work will start week of 9/8. Working on bridge foundations. Pavement work has restarted. Opened University Parkway Ramps. Working on Red Bank & Rosenberger Southern Approaches. Continuing to work on bridges and Eastbound Pavement. **One Bridge deck pour left, working on approach slabs and curb pours.**
1900262			SR 62 At 6.62 mi W of US-41 (Schutte Rd)	Intersection Improvement				Complete					
1900264			SR 62 At 4.58 mi W of US-41 (Rosenberger Ave)	Intersection Improvement				Complete					
1900308			SR 62 From Rosenberger Rd (4.59 mi W of S Jct US-41) to 3.92 mi W of S Jct US-41 (Ingle Ave)	Road Reconstruction (3R/4R Standards)				Complete					
2001917			SR 62 From 8.56 mi W US 41 to 4.59 mi W of US 41 (East of Posey/Vanderburgh Count Line to Rosenberger Rd	Rubblize PCCP & HMA Overlay				Complete					
2100041			SR 62 At McDowell Road, 7.75 mi W of US41	Intersection Improvement				Complete					
2201132	R-44695	Hill, Luke	SR 68 From 1.2 mi E. US 41 to 4.0 mi W. of SR 61 intersection on SR 68 (RPs 23.2, 31.59 and 31.79)	Small Structures & Drains Construction	Complete	Complete	N/A	Complete	N/A	Complete	3/12/25	On-Going	**Awaiting on Pre-Final for the completed construction.**
1701058	R-40551	Risse, Dakota	SR 62, various locations between SR 61 and the West Jct SR-161	Small structure replacements	7/31/2018	8/15/2019	N/A	All approvals done by 9/2/2020	N/A	Complete	3/12/25	On-Going	**SR 62 west of SR 161 is finished with construction and is now open. Closure has moved to SR 261.**
1700170			SR 161 10.46 miles N Jct SR-66	Small Structure Replacement									
1702071			SR 62 04.79 mile E SR-61	Small Structure Replacement									
1702072			SR 62 3.88 mile E, W Jct SR-161	Small Structure Replacement									
2001938			SR 261 over UNT, 3+70 N JCT SR 66	Small Structure Replacement with Bridge	Complete	Complete	N/A	Complete	N/A	Complete			
1900115			SR 161 Over Coles Creek, 0.69 mi N SR-62	Replace Superstructure	Complete	Complete	Complete	Complete	N/A	Complete			
2100633	B-43972	Lyle, Rachel	SR 61 over CARTER-TRAYLOR DITCH, 00.08 E SR 261	Bridge Thin Deck Overlay	Complete	Complete	Complete	Complete	N/A	Complete	9/10/25	On-Going	Construction is still on-going. Estimated contract completion date of 08/30/2026. **Project delayed due to rain but substantially complete with a Pre Final scheduled for 9/11/26.**
2100634			SR 61 over CYPRESS CREEK, 00.19 E SR 261	Bridge Thin Deck Overlay				Complete					
2100812	R-43982	Sturgeon, Clancy	SR 66 over UNT, 1.45mi E JCT SR 65	Small Structure Pipe Lining	Complete	Complete	N/A	Complete	Complete	Complete	11/13/2025	On-Going	Received Final Tracings Files from Designer, waiting to be reviewed. All files are with Central Office. With Contracts- waiting for Letting on 11/13/25. Has been awarded to E&B Paving, but Pre-construction meeting will not be until late Winter/early Spring. Work likely will not start until HMA plants fire back up next Spring. Pre-Construction Meeting scheduled for 3/9/26. Tentative schedule for the pipe lining is 6/8/26 - 7/1/26 and for the HMA Overlay is 7/8/26 - 10/30/26. **Construction complete on SR 66. SR 57 resurface is actively in construction.**
2100260			SR 57 From 1.32 N. US 41(End of Concrete) to S. Jct. of I 69 (end of Asphalt)	HMA Overlay, Preventive Maintenance									
2002063	B-43235	Lyle, Rachel	SR 68 over MILL CREEK, 00.26 E SR 61	Bridge Replacement	Complete	Complete	Complete	Complete	Complete	Complete	11/13/25	On-Going	Construction has commenced and still on-going. Estimated contract completion date of 09/01/2026. **Finishing up construction with Pre Final scheduled for 9/9/26.**
2100668	B-43969	Risse, Dakota	I 64 EBL over CR 100 W, 01.92 E SR 61	Bridge Deck Overlay	Complete	Complete	N/A	Complete	N/A	Complete	12/10/25	On-Going	Awarded to E & B paving. Pre-construction meeting held on 02/26/26. **Construction should be complete no later than the end of September 2026.**
2100669			I 64 WBL over CR 100 W, 01.92 E SR 61	Bridge Deck Overlay				Complete					
2100717			I 64 EBL over TRIB. OF COLES CREEK, 06.74 E SR 61	Bridge Deck Overlay				Complete					
2100718			I 64 WBL over TRIB. OF COLES CREEK, 06.74 E SR 61	Bridge Deck Overlay				Complete					

					Preliminary Engineering/ Design				Right-of-Way	Design	Construction		
Des	Contract	Project Manager	Project	Description	Consultant Selection & NTP	Preliminary Field Check	Public Hearing / Meeting Notice	Environmental Approval	Right of Way Acquisition	Final Tracings	Bid Letting/ Award	Construction	Most Current Status Information
2301254	R-45152	Sprinkle, Emily	SR 62 from 3.92 mi W of S Jct US 41 (Ingle Ave) to 2.72 mi W of Jct US 41 (Wabash Ave)	Pavement Replacement	Complete	Complete	Complete	Complete	Complete	Complete	2/11/26		New contract, separated Des from the larger Lloyd project R-42287 to allow for Utility Relocations. Public Hearing held 9/26/23. Working to determine lighting locations with City of Evansville. Working on Stage 3 plans, revising utility agreements, and finalizing utility conflicts. Final Field Check was held. Working through a couple utility conflicts and gather the last few utility workplans. Utility relocations are ongoing. Final Tracings have been sent to Central Office. Waiting on letting. Utility relocations ongoing. Waitng for Notice to Proceed be issued to contractor. Pre-construction conference was held. Waiting to receive start date from contractor. **Utility relocations are underway. Construction start has been pushed to October after the Fall Festival.**
1900263			SR 62 At 3.09 mi W of US-41 (St. Joseph Ave.)	Intersection Improvement									
2000187			SR 62 2.72 mi W of US 41 (Wabash Ave)	Intersection Improvement									
2200518	R-44505	Robbins, Stephen	I 64 From 3.32 miles E of SR 65 interchange to 1.69 miles W of SR 37 interchange	Small Structures & Drains Construction	Complete	Complete	Complete	Complete	N/A	On-Going	*11/5/26*		Environmental documentation is complete. Final Field Check held 6/16/26. Stage 3 design is complete. **Obtained permits 8/26/26. Working on Final Tracings. Will let without exceptions.**
2200037	R-45753	Hill, Luke	US 41 0.66 miles S. of SR 57 at St. Petersburg Rd	Intersection Improvement	Complete	N/A	On-Going	On-Going	On-Going		*4/7/27*		**Project is going to be moved to an April 2027 letting due to the railroad coordination being incomplete and awaiting on agreements to be signed.**
2200972	R-44506	Hill, Luke	I 64 From 0.82 miles E of SR 65 to 0.96 miles E of SR 65	Slide Correction	Complete	Complete	N/A	Complete	Complete	On-Going	*12/9/26*		RIprap alternative is selected for the slide correction. **Final Tracings were submitted and are in the process of being reviewed.**
2100044	R-44013	Hill, Luke	SR 62 (Morgan Ave.) At Boeke Road, 1.01 mi E of US 41	Intersect. Improv. W/ Added Turn Lanes	Complete	2/15/2024	N/A	On-Going			*2/10/27*		**A tree is going to get put on a maintenance contract and will be cut down this November. Utility relocations will follow tree removal. Will have to let with utility exceptions. Working towards final tracings on Boeke. On Stockwell, we are waiting for the liquor store to move their sign (by September 1st). Working towards final tracings. Clearing up cost to cure. Right-of- way concerns with Boeke and Stockwell.**
2100051			SR 62 At Stockwell Road, 2.01 mi E of US 41	Intersect. Improv. W/ Added Turn Lanes				On-Going					
2300807			SR 62 SR 62 Bridge over HARPER DITCH, 01.78 mi E US 41	Bridge Deck Overlay	Complete	Complete	Complete	On-Going					
2301147	R-45274	McCormick, Katie	From 3.30 mi N SR-57 (0.20 mi N Boonville/New Harmony Road) to 0.85 mi S. SR 168 (0.20 mi N. Coal Mi	Rubblize PCCP & HMA Overlay	Complete	On-Going	On-Going	On Going			*8/11/27*		**Resubmitted to Cultural Resource office on 7/2 and comments anticipated back by 7/24. Expedited review request submitted 7/29 and asks for Arch review complete by 8/4. Utility conflict analysis and Subsurface Utility Engineering (SUE) field work is in progress. Additional SUE has been requested from Central Office SUE on-call. Bi-weekly reoccurring meeting with Evansville water and sanitary is ongoing. All workplans have been requested. Submit notice for a public hearing once MPPA (environmental) is approved and Categorical Exclusion (CE-3) has been released for Public Involvement. Continue Right-of-Way engineering. Environmental comments received and revisions in progress. Resubmitted to Cultural Resource Office on 8/7 and comments anticipated back by 8/28. Expedited review request submitted 7/29. Hold Traffic Management Plan stakeholder meeting after Request for a Public Hearing is complete.**
2500077			From 3.30 mi N SR-57 (0.20 mi N Boonville/New Harmony Road) to 0.85 mi S. SR 168 (0.20 mi N. Coal Mi	Small Structures & Drains Construction	Complete	On-Going	On-Going	On-Going					
2200649			US 41 NB over Pond Flat Ditch 02.01 miles S of I-64	Bridge Replacement	Complete	N/A	N/A	On-going	On-Going				
2200650			US 41 SB over Pond Flat Ditch 02.01 miles S of I-64	Bridge Replacement				On-Going					
2301241	R-45295	Robbins, Stephen	SR 66 From 1.81 mi E of US 41 to 1.91 E of US 41 (EB)	Bike/Pedestrian Facilities	Complete	Complete	Complete	On-Going			*9/15/27*		Notice to Proceed issued. Survey is complete. Working on Red Flag Investigation and on Stage 1 design. Stage 1 is complete. Working on environmental field work and pedestrian maintenance of traffic options. Received Stage 1 comments back. Finalizing Right-of-Way limits and continued work on environmental. Preliminary Field Check was held, addressing comments. Working on getting approval from the Technical Advisory Committee to make sure everything is ADA compliant. Continuing work on environmental. Right-of-way has moved to appraising. Stage 2 due mid-May. Working on pedestrian maintenance of traffic. Stage 2 has been submitted and comments were received. Temporary Occupancy Letter has been sent to the City of Evansville for approval.

					Preliminary Engineering/ Design				Right-of-Way	Design	Construction		
Des	Contract	Project Manager	Project	Description	Consultant Selection & NTP	Preliminary Field Check	Public Hearing / Meeting Notice	Environmental Approval	Right of Way Acquisition	Final Tracings	Bid Letting/ Award	Construction	Most Current Status Information
2200038	R-44500	Risse, Dakota	SR 66 2.23 miles W of SR 65 at University Parkway Intersection	Intersection Improvement	Complete	On-Going		On-Going			*9/15/27*		For University Parkway working through environmental comments. **Stage 2 review complete.** For SR 57 in Daylight, confirmed with the county to use Boonville-New Harmony road a detour route. Maintenance of Traffic is to be a closure with business access. Stage 2 is complete under consultant review. **SR 57 Public information meeting held on 08/12/2026.**
2301075			SR 57 3.36 mi S of I-69 (N. Green River Rd. Intersection)	Intersection Improvement	Complete	On-Going		On-Going					
2400696			SR 57 3.36 mi S of I-69 (N. Green River Rd. Intersection)	ADA Sidewalk Ramp Construction	Complete	On-Going		On-Going					
2301164	R-45284	Hill, Luke	From 0.47 miles N of SR 68 to 1.93 miles S of SR 64	Small Structures & Drains Construction	Complete	Complete		On-Going			*9/15/27*		Preliminary Field Check was held on 4/9/26. Environmental Document in progress. Prepared formal hydraulic reports for each location and waiting for INDOT Hydraulics for liner option approval. Working on Stage 2 documents ahead of hydraulic approval to keep the project moving forward.
2200684	B-44509	Sturgeon, Clancy	SR 57 01.08 miles S of I-69	Bridge Rehabilitation Or Repair	Complete	Complete	N/A	On-Going	On-Going		*1/12/28*		Waiting on the Subsurface Utility Engineering to proceed with Utility Coordination. Continuing through the process of the Environment document. After a recent crash, INDOT has requested widening the exisiting structure to provide additional stopping sight distance and recovery which was outside the original scope. Supplemental submitted as this will make modifications to the Environmental document, the design and plans. No New Updates. Historic Bridge Alternative Analysis re-submitted to INDOT for review on 12/4/25. 60% plans to be submitted in the next few weeks. **Historic Bridge Alternative Analysis and 60% Plans submitted for review on 5/8/2026 and still waiting for comments. Held meeting with Consultant and Tech Service team to discuss the consideration to implement a 4-way stop at SR 57/Baseline Road Intersection.**
2500475	T-46548	Risse, Dakota	Various locations(Vanderburgh and Warrick Counties)	Traffic Signals Moderinization	Complete	On-Going					*2/9/28*		Being designed in-house at Central Office. Working towards a high level Stage 1 plan submittal.
1601011	R-39923	Hill, Luke	US 41 At Lynch Road, 1.0 mi N of SR-66	Intersection Improvement. Added left turn lane on SB US 41. No improvements on Lynch other than resurface.	Complete	Complete	None	CE1 9/17/2019	N/A		*11/15/28*		We just had a kick-off meeting to make sure everyone is on the same page and restarting all the coordinations (Railroad, Right of Way, and Utilities). Working on a "dummy" stage 2 submittal before jumping into Stage 3 design. Continued work on the scope and drainage of the project. Discussion taking place about the current estimate of the project. **Field work and waters recheck has been completed and a new Waters Report is in process. Pavement design is in process.**
2401422	R-45930	Robbins, Stephen	From 4.3 mi W. SR 65 (Beginning of 4 Lane Section) to 2.11 mi E. SR 65	Small Structures & Drains Construction	Complete	On-Going					*11/15/28*		Working on Survey. Notice to Proceed received on 12/31/25. Currently working on Stage 1 design.
2401495	R-45762	Risse, Dakota	Concrete Pavement Restoration (CPR)	I 69 I 69 From Jct. SR 66 to I-64	Complete	On-Going							This project includes 8 bridge deck overlays and 14 small structures along I-69. We have had an initial field check on the bridge projects as of 12/17/2025. In the early stage of development, intitial work on-going. **Stage 1 documents have been submitted and reviewed. Continue on working through comments.**
2401528	R-45795	Hill, Luke	US 41 1.09 mi N of I 69 interchange (Covert Ave)	Intersection Improvement	Complete	On-Going	On-Going	On-Going	On-Going		*2/14/29*		**Work continues on the development of the engineers report document. Refined cost estimates have been developed for the RCUT and quadrant roadway intersection. Additionally, the requested conflict point X exposure analysis was developed for the quadrant roadway option. The result of this analysis did not result in a reduction of conflict points for the quadrant roadyway option. David Reamer is reviewing the analysis to confirm. A meeting to discuss the preferred alternative will be scheduled as well as a field meeting. Red Flag Investigation and final Section 106 fieldwork day 8/20/2026. Followed-up with utility companies that have not yet responded to the Initial Notice Request and sent out Verification Request.**
2401531													
2300710	R-45035	Hill, Luke	SR 62 1.50 mi W of I-69 (Green River Rd.)	Other Intersection Improvement	Complete	Complete					*7/11/29*		Waiting on Notice to Proceed. Held initial field check and project kick-off meeting. Finishing up survey and starting to put prelimiary plans together. Geometric review is complete, working on addressing comments. **Stage 1 plans were submitted on 8/21/26 and we are in process of scheduling a TAC meeting. UAV photos were taken for future public involvement. Right-of-Way and Land Acquisition process has started.**
2500772	B-46286	Lyle, Rachel	US 41 over UNT, 0+08 N JCT SR 57 Structure #: CV 041-082-09.04 NBL	Small structure replacement with bridge	On Going						*7/11/29*		Waiting on INDOT Contracts department for fee negotiations and Notice to Proceed. **Contracts negotiations have been sent to Resolution Group to review and for their concurrence. If they agree, the contracts will be sent to contract management for finalization and distribution for signature.**
2500773			US 41 over UNT, 0+08 N JCT SR 57 Structure #: CV 041-082-09.04 SBL										
2500775			US 41 over UNT, 0+79 S JCT SR 57 Structure #: CV 041-082-08.17										

					Preliminary Engineering/ Design				Right-of-Way	Design	Construction		
Des	Contract	Project Manager	Project	Description	Consultant Selection & NTP	Preliminary Field Check	Public Hearing / Meeting Notice	Environmental Approval	Right of Way Acquisition	Final Tracings	Bid Letting/ Award	Construction	Most Current Status Information
2500799	R-46290	Risse, Dakota	SR 66 SR 66 FROM .2mi W of SR 61 TO .2mi E of SR 61	Intersect. Improv. W/ New Signals	Complete						7/11/29		DCCM has been chosen as designer. Fee negotiations complete. **Received notice to proceed. Projects getting underway.**
2500800			SR 66 SR 66 at Bell Road in Evansville	Other Intersection Improvement	Complete								
2500801			SR 62 SR 62 at Epworth Road in Evansville	Intersect. Improv. W/ New Signals	Complete								
2500632	B-46288	Robbins, Stephen	SR 61 over CARTER-TRAYLOR DITCH, 0.08 N SR 62	Thin Deck Overlay	Complete	On-Going					7/11/29		Designing in-house with Mark Williams. Working on Stage 1 design.
2500633			SR 61 over CYPRESS CREEK, 3.10 N SR 62	Bridge Thin Deck Overlay		On-Going							
2500910	R-46328	Risse, Dakota	SR 261 From SR 66 to From 3.01 mi N. SR 66	HMA Overlay, Preventive Maintenance	Complete	On-Going					7/11/29		Being designed in-house at Vincennes. Early in design phase. Finalizing initial scope additions to project.
1802087	T-43506	Risse, Dakota	I 69 ITS-EXP CCTV/DMS from US 41 to SR 68	ITS Traffic Management Systems	On going						9/12/29		Waiting for a designer to be chosen.
2002562			I 64 ITS-EXP CCTV/DMS from SR 65 to SR 161		On going								
1802047	T-41768	Risse, Dakota	I 64 ITS-EXP CCTV/DMS from 3 miles W of SR 69 to 1 mile W of SR 62/64, Excludes Vanderburgh & Warrick Cos	ITS Traffic Management Systems	Complete	N/A	On-Going	On-Going	On-Going		9/12/29		**Stage 2 plans are under review.**
2401393	R-45795	Risse, Dakota	SR 61 4.62 mi S of SR 62 (Roeder Rd./CR 300 S)	Intersection Improvement, Roundabout	On-Going	On-Going	On-Going	On-Going	On-Going		9/12/29		Early Coordination Letters sent out. Working towards a stage 1 submittal. Early concerns with the amount of Right-of-Way involved. **Held a preliminary geometric review meeting with Central Office. Looking at schedule and a second high level stage 1 submittal.**
2200044	R-44499	Hill, Luke	US 41 1.57 miles S of SR 57 At St. George Road	Intersection Improvement	Complete	N/A	On-Going	On-Going	On-Going		10/11/29		Kick-Off Meeting held in November. Early Development for Stage 1 plans and Utility Coordination Meetings are on on-going. Survey is being completed. Met with the Evansville Airport to discuss plans and Right-of-Way. Held meeting with stakeholders across the airport to discuss the traffic flow and maintenance of traffic issues. Project got moved back due to reshuffling taking place Central Office. New letting date is 10/11/2029. Stage 1 has been submitted and reviewed. Stakeholder coordination is on-going. Working through 3 design alternatives to see which would have the best cost-benefit analysis.
2500657	B-46287	Robbins, Stephen	SR 162 over N&S RR, 01.62 E SR 62	Bridge Deck Overlay	On-Going						11/7/29		**Designer has been selected and scoping meeting took place in mid-July.**
2500771			SR 62 over UNT, 2+98 E JCT SR 145	Small Structure Replacement with Bridge									
2500774			SR 545 over , 6+78 S JCT SR 62	Small Structure Replacement									
2500883			From 3.61 miles west of SR 161 to 3.22 miles west of SR 161	Small Structures & Drains Construction									
2500885			From 0.5 Mi E of SR 145 to 0.15 Mi E of SR 37	Small Structures & Drains Construction									
2501051	R-46488	Robbins, Stephen	I-64 from 1.91 mile W SR 161 Overpass to .79 Miles E US 231	HMA Overlay, Preventive Maintenance	On-Going						11/7/29		**Project is just getting started and the consultant just got picked for the project.**
2501068			I-64 from 1.91 mile W SR 161 Overpass to .79 Miles E US 231	Small Structures & Drains Construction									
2500802	R-46285	Hill, Luke	SR 62 at Posey County Line Road	Intersection Improvement	On-going						12/12/29		Project is just getting started and waiting for Notice to Proceed. Starting work on Stage 1 design plans.
2500798	R-46317	Hill, Luke	Walnut St. and Lincoln Ave and Bellmeade Avenue in Evansville	Intersection Improvment	Complete						1/16/30		Developing preliminary layouts for the alternatives. Starting the section 106 for the environmental field work. A meeting will take place to discuss traffic analysis, alternates, crash analysis and cost estimates. Will be scheduling a scoping field check soon. Continued work on utility coordination.
2500823	T-45920	McCormick, Katie	SR 62 FROM 0.0 miles E of US 41 TO 1.0 miles E of US 41	Bike/Pedestrian Facilities	On-Going						1/16/30		Waiting on Consultant to be selected. Scoring is completed, waiting for consultant to receive the selection notification. Scoping meeting is scheduled for July 1st. **Consultant secured. Scoping meeting held / received meeting minutes. Scope and Fee's provided to Central Office.**
2200040	R-45412	Hill, Luke	US 41 At SR 57 Intersection	Intersection Improvement	Complete	Complete	N/A	On-Going	On-Going		1/15/31		Working on lowering the cost of the project. No need for Right-of-Way acquistion nor any utility conflicts. Putting together a traffic study to review to see if the alternative is feasible. Stage 1 plans were submitted in February and continued work on the environmental document. **Preliminary field check took place in August and discussion about utilizing Subsurface Utility Engineering (SUE) to inspect drainage and pipes in the state's Right-of-Way to see if they will need to be added to the project.**

Non-italicized dates reflect the completion date for the activity.
Italicized dates reflect anticipated completion dates for the activity, where appropriate.

Evansville MPO
Henderson • Vanderburgh • Warrick

Pamela Drach
Executive Director

TO: Policy Committee Members
Technical Committee Members

FROM: Pamela Drach, Executive Director

SUBJECT: FY 2026-2030 TIP Modifications

DATE: September 3, 2026

The Evansville Metropolitan Planning Organization processed several modifications to the FY 2026-2030 Transportation Improvement Program (TIP) as per the attached spreadsheet. The modifications are informational items for the September 10, 2026 Policy and Technical Committee meetings.

PD/ES

Attachment

2026-2030 TIP Modifications - FHWA

Date Processed	Sponsor	Contract	Des#/ID#	Road	Description	County	Work Type	Funding Type	% Split	Action	Fiscal Year	Phase/ Source	Current TIP Entry	New TIP Entry Total	New TIP Entry Federal	New TIP Entry State/Local
													All amounts in thousands			
20-Jul-26	INDOT	45753	2200037	US 41	at Petersburg Rd	Vanderburgh	Intersection improvement with added turn lanes and signals	HSIP, NHPP	90/10	Move FY	2026	RW	$50	$0	$0	$0
											2027	RW	$0	$50	$45	$5
5-Aug-26	KYTC	N/A	02-383.2	Watson Lane	from Sunset Ln to Green River Rd	Henderson	Reconstruction project and improve safety and reduce congestion on Watson Lane.	STBG	80/20	Revise funding & move FY	2026	CN	$2,300	$0	$0	$0
											2027	CN	$0	$3,030	$2,424	$606
	KYTC	N/A	02-22333	KY 425	from milepoint 0 to 4.747	Henderson	Address pavement condition: Pavement rehabilitation, grinding and patching as needed.	STBG	80/20	Revise funding	2027	PE	$300	$480	$384	$96
											2027	CN	$5,700	$5,520	$4,416	$1,104
19-Aug-26	INDOT	45274	2301147	US 41	3.3 miles N SR 57 to 0.85 mi S SR 168	Vanderburgh/ Gibson	Pavement Replacement	NHPP	80/20	Increase Funding	2028	CN	$55,700	$62,700	$50,160	$12,540
		Includes Des #s: 2200033, 2200649, 2200650, 2301093, 2500077, 2500089, 2500826, 2500827, 2500828, 2501079, 2501080, 2501081, 2501082									2029	CN	$73,500	$84,500	$67,600	$16,900
	INDOT	44365	2200945	Various	Various locations in the Vincennes District	Various	Traffic Signals Modernization	HSIP	90/10	Increase Funding	2027	CN	$1,168	$1,548	$1,393	$155
		Includes Des# 2200945														
	INDOT	46922	2600931	Various	Various locations in the Vincennes and Seymour districts	Various	Repair or Replace Lighting	HSIP	90/10	Add Project	2027	CN	$0	$88	$79	$9
		Group Project: Traffic Signal and Lighting System Improvements														

2026-2030 TIP Modification - Transit

Date Processed	Sponsor	Des#/ ID#	Work Type	County	Description	Action	Fiscal Year	Funding Type	Current TIP Entry	New TIP Entry		
										Total	Federal	State/Local
									All amounts in thousands			
21-Aug-26	HART	N/A	Operating Assistance	Henderson	Includes fixed route operating, preventive maintenance, and ADA complimentary paratransit service	Revise Funding	2027	5311	$2,008	$1,206	$603	$603
	HART	N/A	Administrative Assistance	Henderson	Superintendent and Clerical Salaries and Overtime	Revise Funding	2027	5311	$350	$333	$266	$67
	HART	N/A	Planning Assistance	Henderson	Planning Assistance	Revise Funding	2027	5304	$13	$25	$20	$5
							2028	5304	$13	$25	$20	$5
							2029	5304	$13	$25	$20	$5
							2030	5304	$13	$25	$20	$5

Evansville MPO
Henderson • Vanderburgh • Warrick

Pamela Drach
Executive Director

TO: Policy Committee Members
Technical Committee Members

FROM: Pamela Drach, Executive Director

SUBJECT: FY 2026-2030 TIP Amendments

DATE: September 3, 2026

The Evansville Metropolitan Planning Organization is seeking approval of the attached amendments to the 2026-2030 Transportation Improvement Program (TIP). A public review and comment period was publicized for August 26, 2026 through September 9, 2026. The TIP Amendments are an action item for the September 10, 2026 Policy and Technical Committee meetings.

PD/ES

Attachment

2026-2030 TIP Amendment: September 10, 2026

Sponsor	Contract	Des#/ID#	Road	Description	County	Work Type	Funding Type	% Split	Action	Fiscal Year	Phase/ Source	Current TIP Entry	New TIP Entry		
													Total	Federal	State/Local
												All amounts in thousands			
KYTC	N/A	02-2091.10	US 41	bridge over the Ohio River	Henderson	Bridge Project	BR	80/20	Revise funding and move FY	2030	PE	$0	$3,405	$2,724	$681
										2026	CN	$3,000	$0	$0	$0
										2029	CN	$1,000	$0	$0	$0
										2030	CN	$0	$22,700	$18,160	$4,540
KYTC	N/A	02-80309	IC-8029	New Park Entrance	Henderson	Construct a new route into the park from Watson Ln	SPP	80/20	Revise funding and move FY	2026	RW	$300	$0	$0	$0
										2029	RW	$0	$300	$240	$60
										2026	U	$50	$0	$0	$0
										2029	U	$0	$250	$200	$50
										2027	CN	$2,900	$0	$0	$0
										2030	CN	$0	$2,900	$2,320	$580
KYTC	N/A	02-80310	KY 425	from US 60 to US 41	Henderson	Improve level of service on KY 425 from US60 to US 41	SPP	80/20	Move FY	2027	PE	$1,740	$0	$0	$0
										2029	PE	$0	$1,740	$1,392	$348
										2029	RW	$660	$0		
										2030	RW	$0	$660	$528	$132
										2029	U	$470	$0	$0	$0
										2030	CN	$30,160	$0	$0	$0
KYTC	N/A	02-80311	US 60	at KY 1078	Henderson	Improve eastern intersection of US 60 and KY 1078	SPP	80/20	Move FY	2027	PE	$270	$0	$0	$0
										2029	PE	$0	$270	$216	$54
										2028	RW	$390	$0	$0	$0
										2030	RW	$0	$390	$312	$78
										2028	U	$440	$0	$0	$0
										2029	CN	$1,620	$0	$0	$0
KYTC	N/A	02-80350	KY 812	at the Sports Complex MP5.7 to 6.11	Henderson	Improve congestion and mobility on KY 812 in the vicinity of the sports complex.	SPP	80/20	Revise funding and move FY	2029	PE	$0	$520	$416	$104
										2026	RW	$100	$0	$0	$0
										2030	RW	$0	$300	$240	$60
										2026	U	$250	$0	$0	$0
										2026	CN	$1,000	$0	$0	$0
										2027	CN	$1,000	$0	$0	$0
INDOT	45291	2600670	SR 62	from 6.90 miles E of SR 69 to 7.4 miles E of SR 69 (St Phillips Road)	Posey	Intersection Improvement Median U Turn	HSIP	90/10	Add project	2027	PE	$0	$1,360	$1,224	$136
		Includes Des #s 2200039, 2600705													
INDOT	46285	2500802	SR 62	at Posey County Line Road	Vanderburgh/ Posey	Intersection Improvement Median U Turn	HSIP	90/10	Increase funding	2027	PE	$511	$1,239	$1,115	$124

Pamela Drach
Executive Director

TO: Policy Committee Members
Technical Committee Members

FROM: Pamela Drach, Executive Director

RE: FY 2032 Call for Projects for Indiana LPAs

DATE: September 3, 2026

On July 22, 2026, the Evansville MPO announced a Call for Projects for FY 2032 for Indiana LPAs. Six applications were received and reviewed following the project selection process guided by the Goals and Objectives in the MTP 2050. The following provides a summary of the recommended projects for each LPA that applied for MPO funding:

Project	LPA	Proposed Program Year
Libbert Road (High Pointe Dr to Telephone Rd)	**Warrick County**	**FY 2032**
	The proposed project will include road widening with added lanes, curb and gutter, and additional storm sewer improvements with sidewalks and bike lanes, or possibly a bike trail, along one side of the shoulder.	
Hogue Rd Bridge #860 Replacement (at Carpentier Creek)	**Vanderburgh County**	**FY 2032**
	The proposed project will replace the existing two span bridge with a single span structure, also including approach work on the east and west sides of the structure.	
SR 662 / Yorkshire Dr / Frame Rd Roundabout	**Newburgh**	**FY 2035**
	The proposed roundabout will replace the existing 2-way, stop-controlled intersection with a single-lane circulatory roadway. Each of the four legs will contain one approach lane and one receiving lane with splitter islands and pedestrian crosswalks, ADA ramps, and sidewalks.	

Your approval designates these projects for MPO funding. The federal participation level and confirmation of programed fiscal year for these projects will be determined as part of the upcoming Transportation Improvement Program (TIP) development process.

This is an action item for the Policy and Technical meetings.

PD/ES

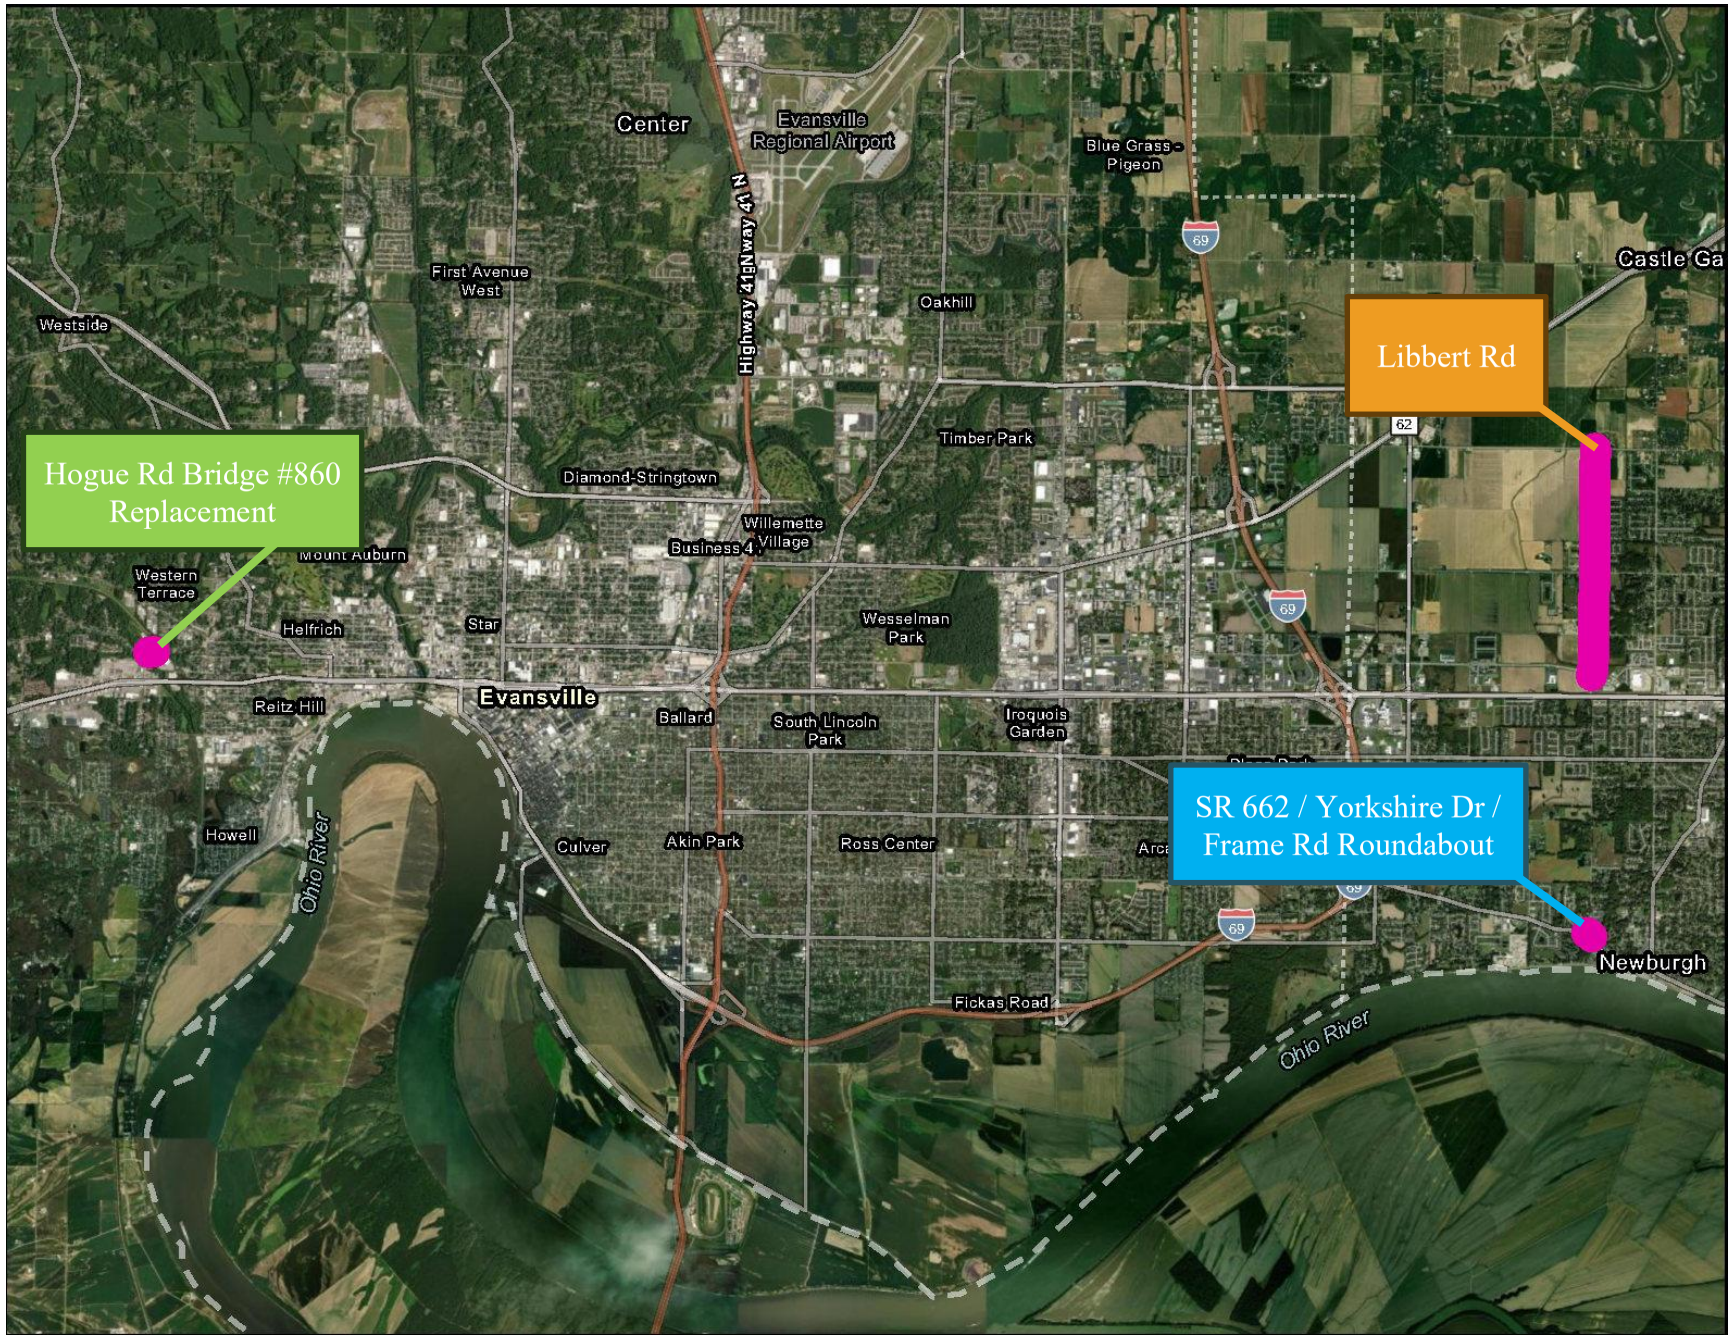
Hogue Rd Bridge #860 Replacement
Libbert Rd
SR 662 / Yorkshire Dr / Frame Rd Roundabout
Center
Evansville Regional Airport
Blue Grass - Pigeon
Castle Ga
First Avenue West
Highway 41N
Oakhill
Westside
Timber Park
Diamond-Stringtown
Willemette Village
Business 41
Mount Auburn
Western Terrace
Helfrich
Star
Wesselman Park
Evansville
Reitz Hill
Ballard
South Lincoln Park
Iroquois Garden
Howell
Ohio River
Culver
Akin Park
Ross Center
Fickas Road
Newburgh
Ohio River
69
62

Regional Mobility Statistics
Transit

2025/2026 FIXED ROUTE RIDERSHIP

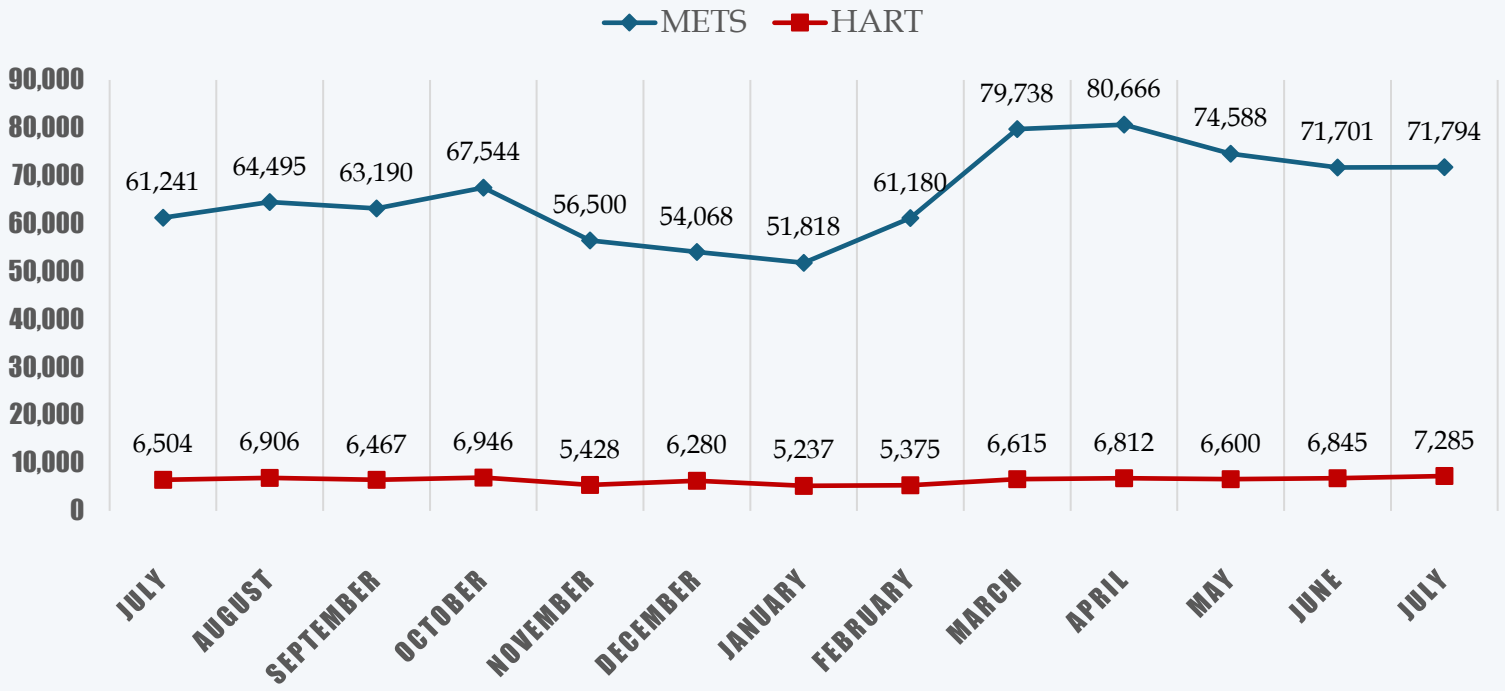

2025/2026 ON-DEMAND RIDERSHIP

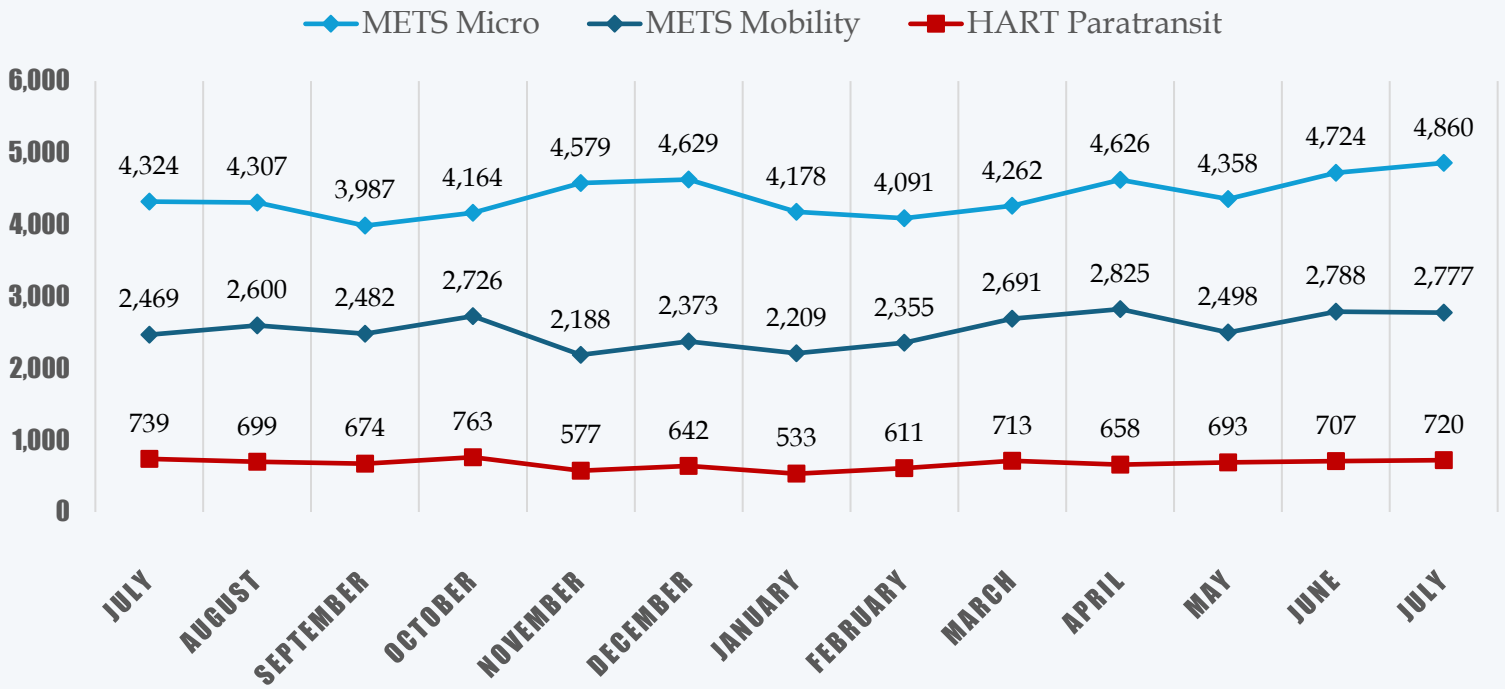

Regional Mobility Statistics
Bikeshare & Scooters

2025/2026 BIKESHARE

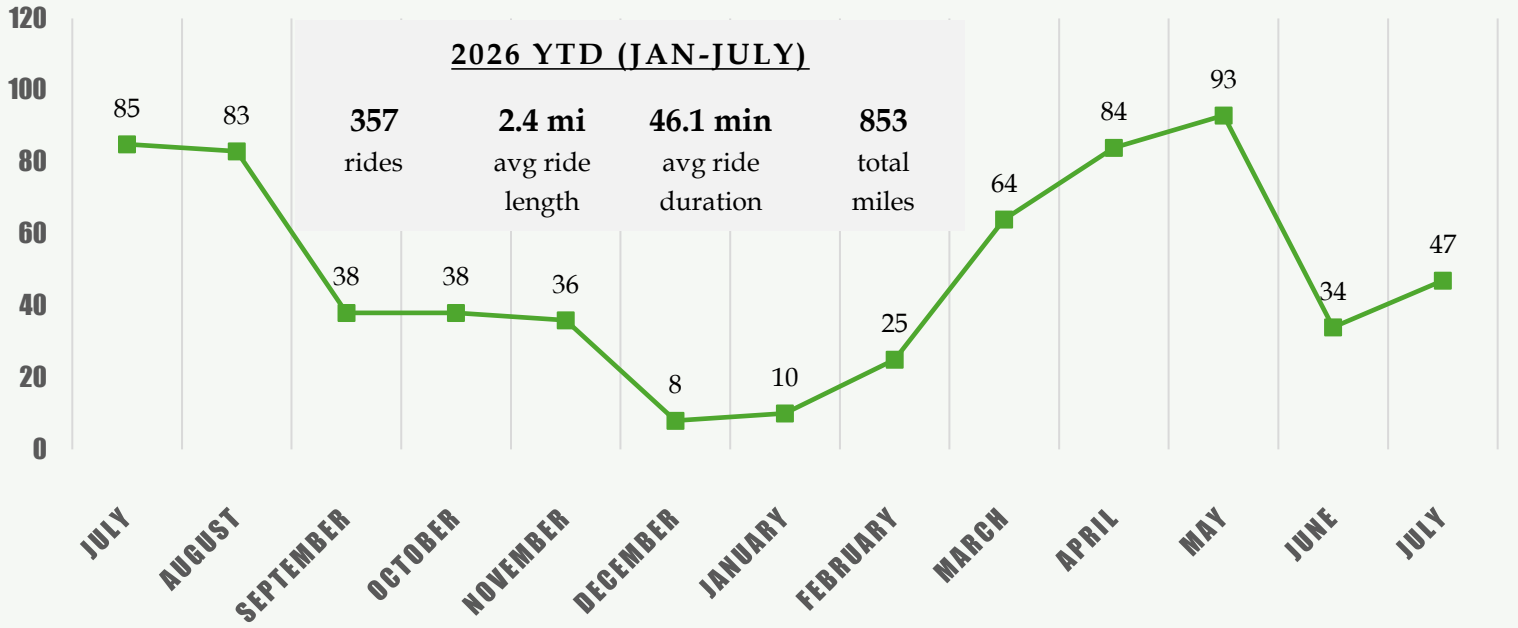

2026 YTD (JAN-JULY)

357	2.4 mi	46.1 min	853
rides	avg ride length	avg ride duration	total miles

2025/2026 SCOOTERS

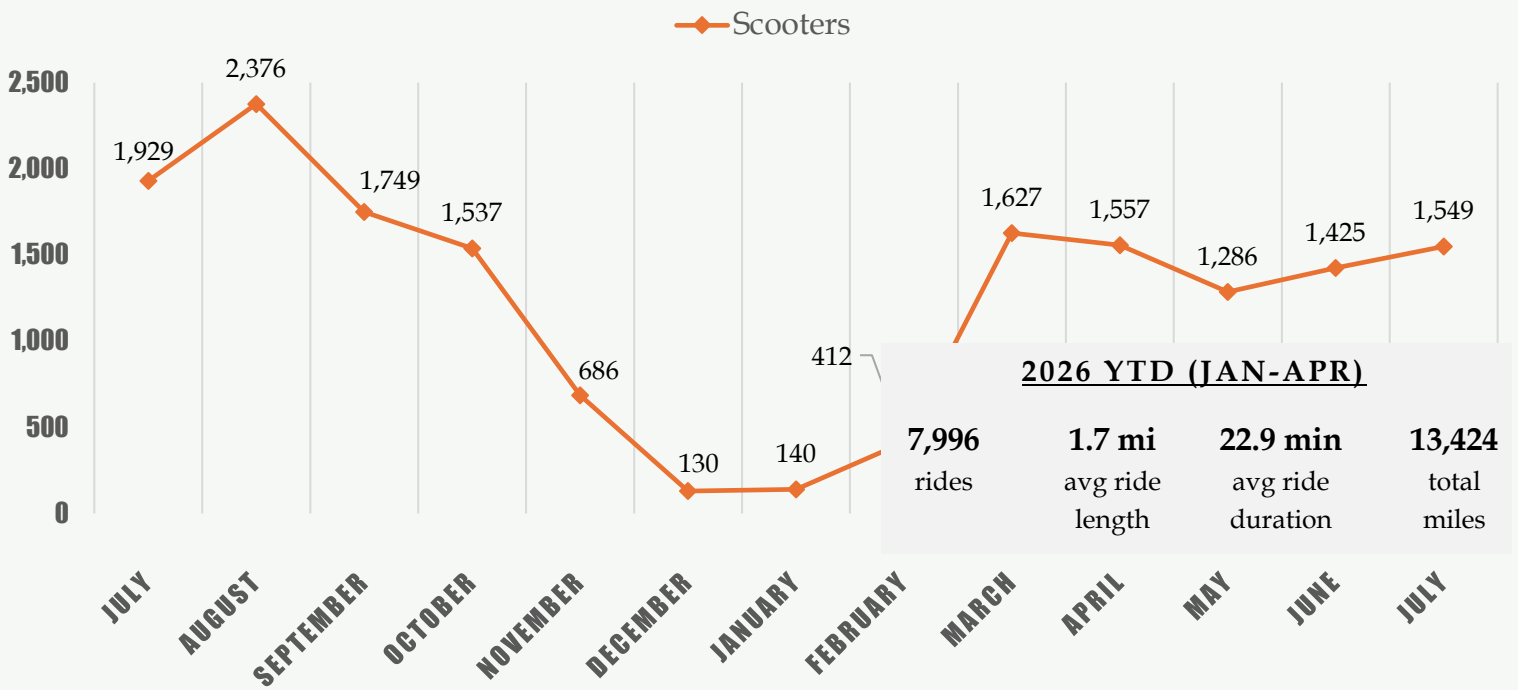

2026 YTD (JAN-APR)

7,996	1.7 mi	22.9 min	13,424
rides	avg ride length	avg ride duration	total miles
